

Project	Enning Route B & C FTTH Upgrade 2023			
Contract No.	T23001			
Contract Date	1/5/2023			
Original Contract Price	\$ 3,330,205.98			
	Contract Price as Amended	Construction Miles	Construction Days	Service Entrances
Contract With Approved Amendments	\$ 4,699,254.46	198.79	120	148
Construction Released w/CAFs	\$ 4,699,254.46	198.79	120	148
Released Construction Miles	198.79	Construction Start Date:	Orig. Compl. Date:	Rev. Compl. Date:
Released Subscriber Entrances	148	5/2/2023	9/20/2023	11/7/2023
Released HBFO Splice Cases	223			
Total Frame Count Fibers	336			
Calculation of Construction Days		Days Startup		
	120	Days Rural Construction		
		Days Town Construction		
		Days Cleanup		
	120	Total Construction Days		
	1.66	Average Miles Required per Day		
Projected Route Miles to Date	97.74	miles		
Route Miles Constructed	86.95	miles		
Average Miles Constructed Per Day	1.47	miles		
Percent of Released Miles Completed	43.74%			
Inventory Complete Route Miles	70.82	miles		
Cleanup Complete Route Miles	70.82	miles		
Construction Days used	59	days		
Construction Delay - Rain	13	days		
Holidays or Non-Working Days	31	days		
Construction Days Remaining	61	days		
Percent of Construction Days Used	49.17%			
Service SEBV Installed	47	quantity		
Percent of Service SEBV Installed	31.76%			
Services Drops Installed	47	quantity		
Percent of Released Drops Completed	31.76%			
Percent Fiber Splicing Complete	14.80%			
Percent Fiber Splicing Tested	14.29%			
Percent Miles Inventoried	35.63%			
Delay Causes				
Remarks	See remarks Exhibit A			
Report By:	Heberly			
Report Date:	8/12/2023			

Remarks Exhibit A

Week Ending 8-12-2023 Enning Route B & C FTTH Upgrade 2023:

Equipment on-site:

- L&P Underground:
 - (1) Vermeer 24x40 directional drill

- MasTec:
 - (1) Dresser TD20 cable plow with Dresser TD20 lead dozer, (2) Case 580S backhoes and (1) CAT 420 backhoe
 - John Deere 450J clean-up dozer
 - Vermeer T655 rock saw
 - John Deere 333G skid steer with Harley-rake attachment
 - Vermeer 1250 cable plow

Construction work completed:

- Zero (0) BHF(24x36x30)T handholes set
- 0.12 mi (652 ft) of BFO 12

Incidents:

- No incident to report.

Project:


- Sub routes ready for splicing include: B1 (Enning), B3, B3A, B4, and B6.
 - 12 splice cases for these areas

Weekly totals:

- **Total BFO was 0.12 mi (652 feet).**
- **Total SEBV for the week was 0.61 mi (3220 feet).**
- **SEBV was installed to eighteen (18) subscriber locations.**
- **Drops were pulled to eighteen (18) subscriber locations.**

Enning Route B

Redowl

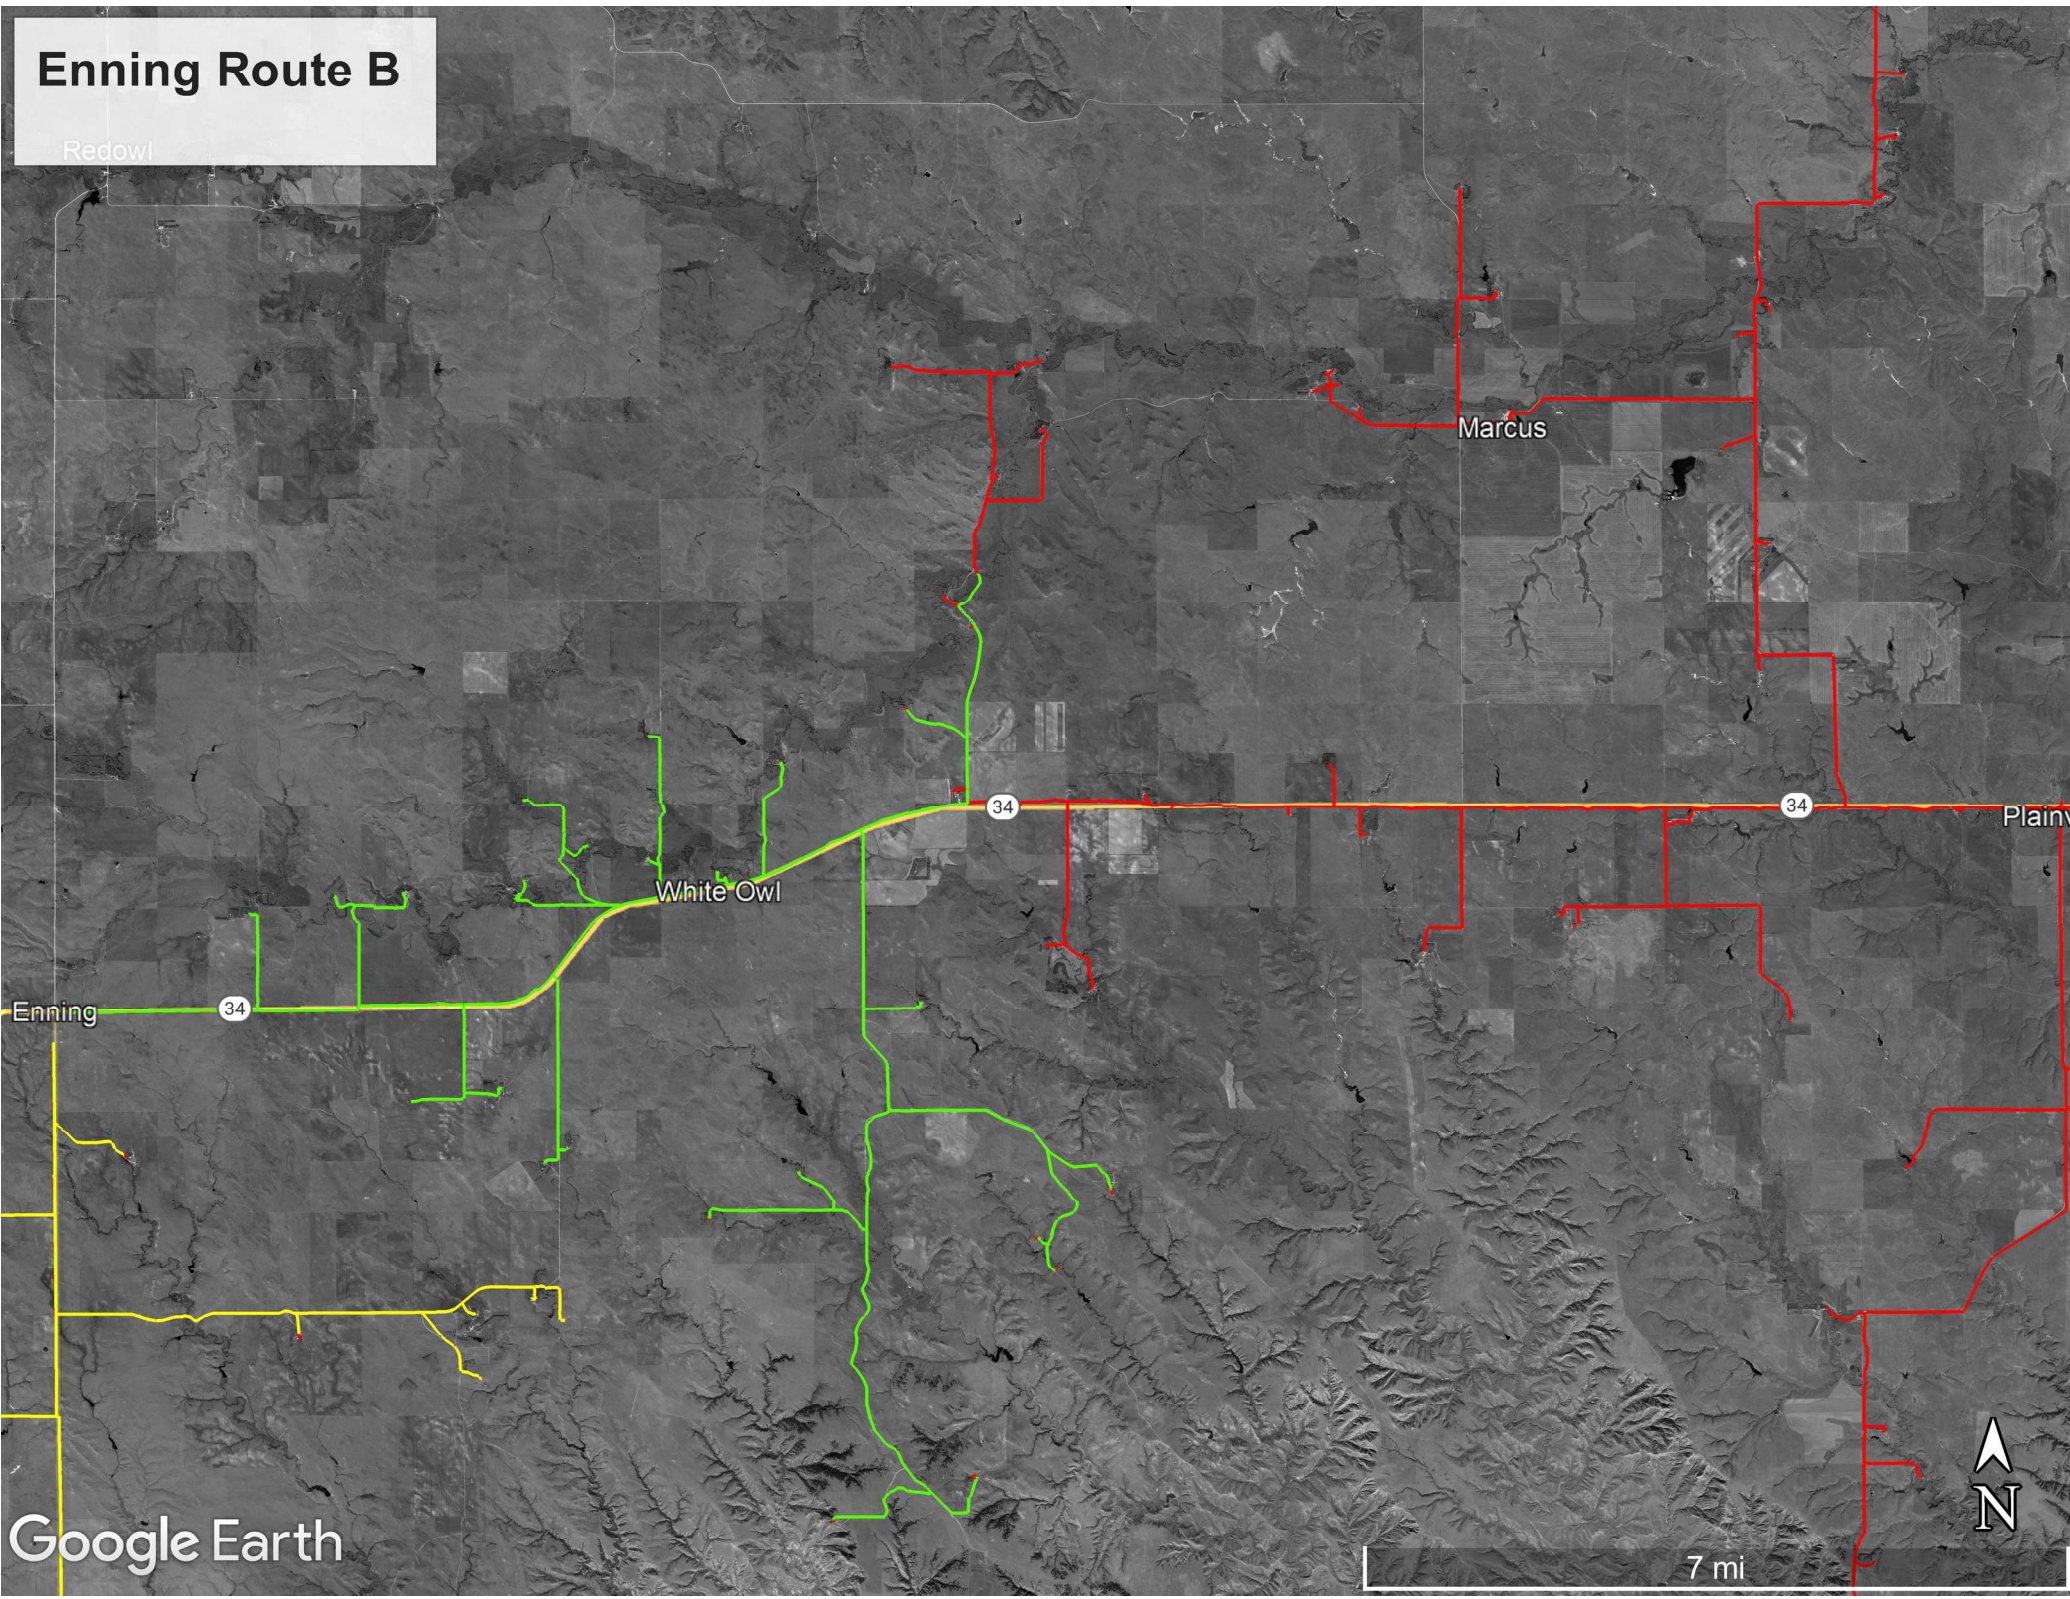

Google Earth

7 mi



Project	Maurine FTTH Upgrade 2023			
Contract No.	T24001			
Contract Date	01/05/23			
Original Contract Price	\$ 2,824,532.85			
	Contract Price as Amended	Construction Miles	Construction Days	Service Entrances
Contract With Approved Amendments	\$ 3,800,686.03	185.68	120	97
Construction Released w/CAFs	\$ 3,800,686.03	185.68	120	97
Released Construction Miles	185.68	Construction Start Date:	Orig. Compl. Date:	Rev. Compl. Date:
Released Subscriber Entrances	97	5/2/2023	9/20/2023	10/26/2023
Released HBFO Splice Cases	157			
Total Frame Count Fibers	393			
Calculation of Construction Days		Days Startup		
	120	Days Rural Construction		
		Days Town Construction		
		Days Cleanup		
	120	Total Construction Days		
	1.55	Average Miles Required per Day		
Projected Route Miles to Date	103.67	miles		
Route Miles Constructed	119.74	miles		
Average Miles Constructed Per Day	1.79	miles		
Percent of Released Miles Completed	64.49%			
Inventory Complete Route Miles	58.24	miles		
Cleanup Complete Route Miles	58.24	miles		
Construction Days used	67	days		
Construction Delay - Rain	5	days		
Holidays or Non-Working Days	31	days		
Construction Days Remaining	53	days		
Percent of Construction Days Used	55.83%			
Service SEBV Installed	56	quantity		
Percent of Service SEBV Installed	57.73%			
Services Drops Installed	56	quantity		
Percent of Released Drops Completed	57.73%			
Percent Fiber Splicing Complete	45.22%			
Percent Fiber Splicing Tested	0.00%			
Percent Miles Inventoried	31.37%			
Delay Causes				
Remarks	See remarks Exhibit A			
Report By:	Heberly			
Report Date:	8/12/2023			

Remarks Exhibit A

Week Ending 8-12-2023 Maurine FTTH Upgrade 2023:

Equipment on-site:

- L&P Underground:
 - (1) Vermeer 24x40 directional drill

- MasTec:
 - (1) Cat D7R LGP cable plow with John Deere 950 lead dozer, (1) Case 580S backhoe and (1) CAT 420XE backhoe
 - John Deere 650J clean-up dozer with rake
 - (1) Vermeer 24x40 directional drill
 - (1) Vermeer 10x15 directional drill

Construction work completed:

- Thirteen (13) BHF(24x36x30)T handholes set
- 5.04 mi (26660 ft) of BFO 12
- 7.76 mi (40992 ft) of BFO 24

Incidents:

- No incidents to report.

Project:

- C2A5 and C2A6 routes north and south of Opal school are ready for splicing.
 - 13 splice cases for this area

Weekly totals:

- **Total BFO was 12.81 mi (67652 feet).**
- **Total SEBV for the week was 0.17 mi (940 feet).**
- **SEBV was installed to five (5) subscriber locations.**
- **Drops were pulled to five (5) subscriber locations.**

Maurine Route B

Bixby

Maurine

212

212

212

73

73

Opal



9 mi

